



ERPNext Phase Roadmap + Dependency Map — AMDG / ABES

Phases, sub-phases, status, and hard (Blocked-By) dependencies. Audience: Mike (engagement lead) & Bryan (founder). Generated 2026-06-24.

 Not Started  In Progress  Blocked  On Hold  Deferred  Gating decision  red = Blocked-by

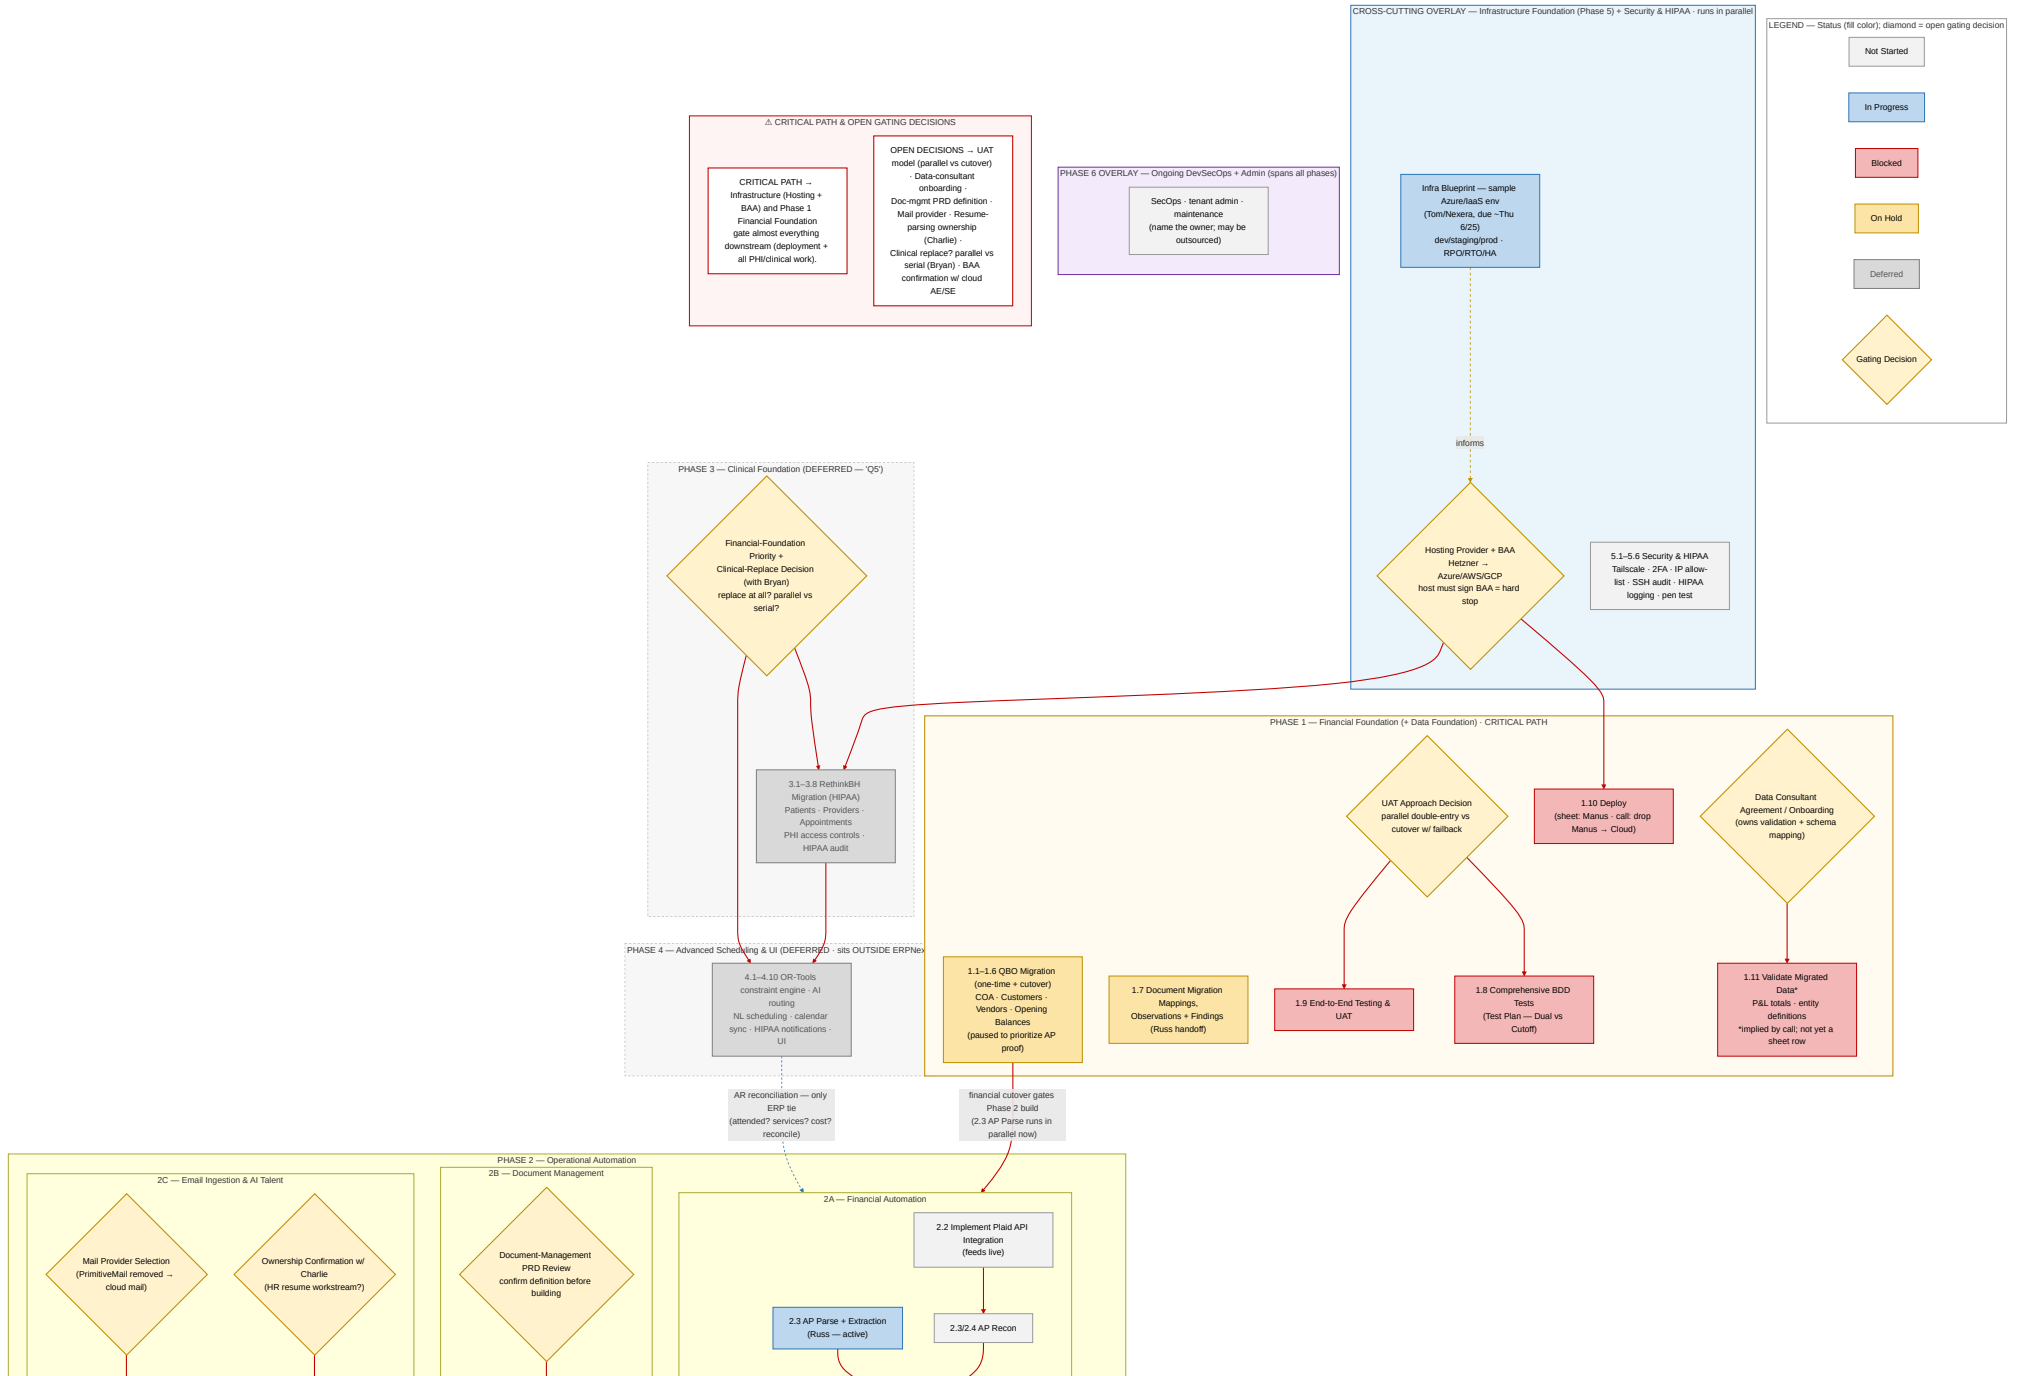



Critical path & open gating decisions

CRITICAL PATH

- Infrastructure (Hosting + BAA) and Phase 1 Financial Foundation gate almost everything downstream — deployment (1.10) and all PHI/clinical work (Phase 3).

OPEN DECISIONS

- UAT model — parallel double-entry vs cutover w/ failback
- Data-consultant agreement / onboarding
- Document-management PRD definition
- Mail provider selection (cloud)
- Resume-parsing ownership (confirm with Charlie)
- Clinical replace at all? parallel vs serial (with Bryan)
- BAA confirmation with cloud AE/SE

Dependency edges (Blocked By → blocked item)

- Hosting provider + BAA → 1.10 Deploy, and all Phase 3 PHI/clinical work
- Infra blueprint (~6/25) → informs the hosting/BAA decision
- UAT approach decision → 1.8 BDD/Test Plan and 1.9 E2E & UAT
- Data-consultant onboarding → 1.11 Validate Migrated Data
- Plaid feeds live (2.2) → AP Reconciliation
- AP parse + recon (2.3) → 2.5 AP BDD Tests
- Document-management PRD review → 2.6–2.9 (Paperless / two-way sync)
- Mail provider selection → 2.10 Mailbox Ingestion
- Ownership confirmation (Charlie) → 2.11–2.13 (resume parsing / AI talent)
- Financial-foundation priority + clinical-replace decision → all Phase 3, downstream Phase 4
- Phase 1 financial cutover → Phase 2 build (2.3 AP Parse runs in parallel now)
- Phase 4 ↔ ERP: AR reconciliation is the only integration tie

Source-of-truth conflicts (flagged, not guessed)

- **No Status/Blocked/Blocked By columns exist.** Built from the workbook "Detailed Tasks" sheet (labels) + the 6/23 call Change Log (statuses). The sheet's only Status column reads "Not Started" for every phase and was not updated post-call.
- **1.7** is "Document Migration Mappings Observations + Findings" (Russ handoff), not "Idempotency & Error Handling".
- **1.10** still reads "Deploy to **Manus**" though the call decided to drop Manus → cloud.
- **1.11 "Validate Migrated Data"** is not a sheet row; implied by the data-consultant decision.
- **Phase 2A:** two rows both numbered **2.3** ("AP Parse + Extraction" and "AP Recon"); **no 2.4** (old Journal-Entry task dropped/merged).
- **5.7 (Hosting+BAA)** and **5.8 (Infra blueprint)** are not numbered rows. Cross-Cutting in the sheet is only 5.1–5.6 (Security & HIPAA) + one unnumbered Infrastructure row; Phases 5 & 6 appear only in the overview.
- **2.10** duplicated in the sheet; collapsed. **2.1** typo'd "Plain" → Plaid.
